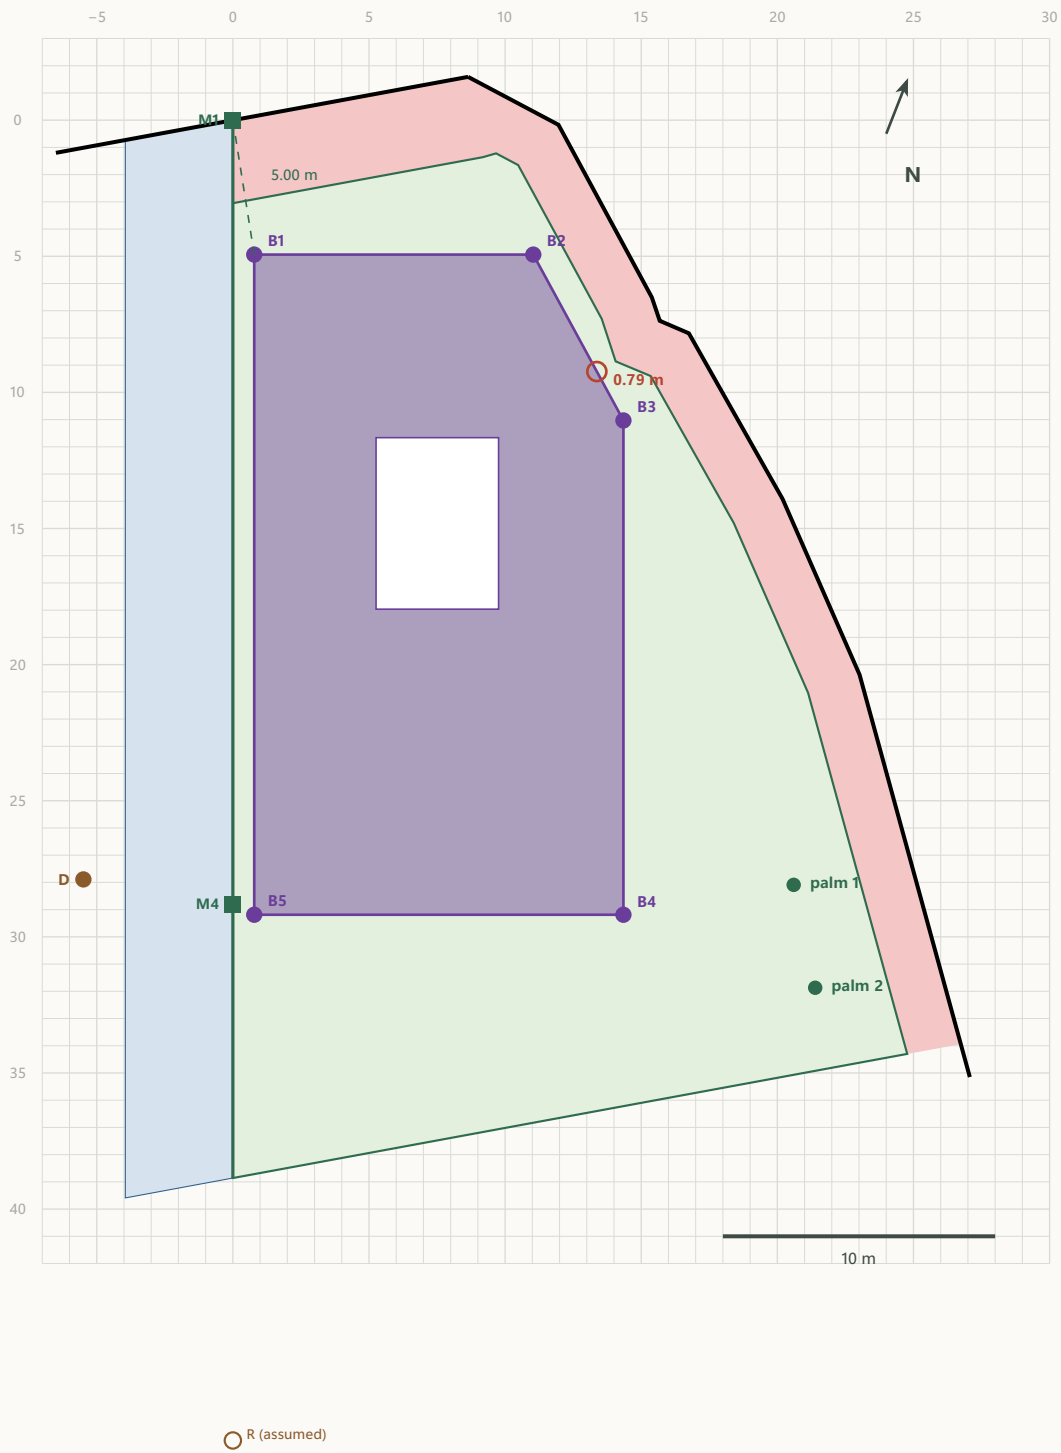


Taif / Palm House

Building test on the land · V8.3 · the house moved south (owner, 4 Nov 2026)

Frame: origin M1 (the gate's east post) · y along the M line southwards · x east, square to it · the house = the room CSVs + (0.91, 5.06) · B1 5.00 m from M1

OK
Every wall inside the envelope with at least 0.50 m spare: the tightest point 0.79 m, on B2–B3 at the lane notch.

Areas

Item	m²
Building outline (outer wall faces)	318.77
Open courtyard	28.35
Roofed ground floor (approx.)	**290.42**
Buildable envelope	667.87
Envelope used by the outline	47.73 %

Checks

Check	Result
Corners outside the envelope (x < 0 = in the driveway)	0
Tightest corner margin (setback or south line)	1.08 m
Tightest point on any wall (edges sampled at 5 cm): B2–B3 at x 13.37, y 9.23	**0.79 m**
the same point square to the lane wall (field check; stop below 2.00 m)	2.97 m
the same point by two tapes: M1 → 16.25, D → 26.53	
Envelope corners poking into the building	0
Palm 1: building to trunk face	5.99 m
Palm 2: building to trunk face	7.27 m
B1 from M1 (the owner's rule: 5.00 m)	5.00 m

First, check the frame on the ground

Base check: M1 → D = **28.43 m** (field 4 Nov 2026: 28.50 m, +0.07 m, accepted). **Re-establish M4** on the M line: from M1 **28.80 m**, from D **5.56 m**. Then tape from M4 to the trunk faces: **palm 1 ≈ 20.35 m**, **palm 2 ≈ 21.34 m**. Within ± 0.3 m → the frame sits on the ground. Corner sheet on page 2; the field instructions in `docs/SITE_SETOUT.md`. The corner margins are for the set-out sheet; the status uses the tightest point on any wall. Every position is to be confirmed by the official survey.

Set-out sheet · tape and string

corners B1… = the outer wall faces of design_gf.typ · reference points M1 and D (M2–M4 are gone)

Method A (two tapes, no square): from M1 and from D, swing the two tapes; where they meet (on the house side, east of the driveway) is the corner.
Method B (string): re-establish M4 (from M1 28.80 m, from D 5.56 m), string M1 → M4, measure **y** along the string from M1, square off with 3-4-5 (3 m along, 4 m out, 5 m diagonal), measure **x** east, drive the peg. Use B to check every corner set out with A, then check the sides and the diagonals.

Corner	x east	y along M	Tape 1 (M1 → m)	Tape 2 (D → m)	Margin to limit	Measured on site	Notes
B1	0.79	4.94	M1 → **5.00**	D → **23.79**	**2.00**		
B2	11.04	4.94	M1 → **12.09**	D → **28.28**	**1.08**		
B3	14.35	11.03	M1 → **18.10**	D → **26.03**	**1.68**		
B4	14.35	29.19	M1 → **32.52**	D → **19.88**	**6.91**		
B5	0.79	29.19	M1 → **29.20**	D → **6.41**	**9.37**		

Side / diagonal	Model (m)	Measured	Difference
B1–B2	**10.25**		
B2–B3	**6.93**		
B3–B4	**18.16**		
B4–B5	**13.56**		
B5–B1	**24.25**		
B1–B4	**27.78**		
B2–B5	**26.33**		

Frame and tightest point	Model (m)	Measured	Difference
M1 → D	**28.43**	28.50 (4 Nov 2026)	+0.07
M4 from M1 / from D	**28.80 / 5.56**		
M4 → palm 1 trunk face	**20.35**		
M4 → palm 2 trunk face	**21.34**		
Tightest point on B2–B3: M1 → / D →	**16.25 / 26.53**		
from it square to the lane wall (stop below 2.00)	**2.97**		
R (assumed) → B5 / B4	19.33 / 24.06 (approx.)		
R (assumed) → palm 1 / palm 2 trunk face	28.73 / 26.83 (approx.)		

Margin = distance to the nearest setback line or the south line (the M line has no setback, so a wall on it is fine): positive = inside by that much; negative = outside. Palms: trunk radius 0.27 m. Peg R is assumed (not in the project files): measure from it to the nearest corners and both palms and record; peg S likewise. Tolerances: the concept accepts ± 0.1 m on a corner and ± 0.3 m on the palms; the official survey fixes the wall faces. Source: base.typ (site baseline v2, field check 3 Oct 2026), design_gf.typ (the house).

Set-out sheet checks: status OK · tightest point 0.79 m on B2–B3 · B1 from M1 5.00 m · palms 5.99 / 7.27 m from the walls.
